



# Weekly Notice of Operations (WNoO)

## Rampion Offshore Wind Farm Limited Construction Operations

Issue Date: 13/04/2018 RAM-ERA-LOG-NOT-0001\_112  
- Weekly Notice of Operations

### Contents

|     |  |    |
|-----|--|----|
| 1)  | Notice to Mariners (NtM) (Active) .....  | 2  |
| 2)  | Hazards/Mitigation for Project Vessels and PAX .....                                   | 2  |
| 3)  | Construction Vessels .....   | 4  |
| 4)  | Guard Vessels .....  | 4  |
| 5)  | Crew Transfer Vessels.....   | 5  |
| 6)  | Upcoming Operations (following 7 days) .....   | 6  |
| 7)  | Summary of Operations (previous 7 days) .....  | 6  |
| 8)  | Looking further ahead (beyond 7 days) (new activities starting) .....                  | 6  |
| 9)  | Project Met mast details.....  | 7  |
| 10) | Project Wave Rider.....  | 7  |
| 11) | As Laid Cardinal Buoy Positions .....  | 7  |
| 12) | Contact details.....   | 7  |
| 13) | Export Cable Coordinates .....   | 8  |
| 14) | New Proposed CR4 Export Cable Coordinates .....  | 10 |
| 15) | Site Chart .....   | 11 |
| 16) | Surface laid export cable and wet stored anchor wire details see update NTM 0096 ..... | 12 |



# Weekly Notice of Operations (WNoO)

## Rampion Offshore Wind Farm Limited Construction Operations

Issue Date: 13/04/2018 RAM-ERA-LOG-NOT-0001\_112  
- Weekly Notice of Operations

WNoO application:

- Issued weekly by the ROW Project Marine Co-ordination Team
- Notice to Mariners (NtM) will be issued for any unplanned/unmarked navigational hazards introduced by the project within our area of operation

### 1) Notice to Mariners (NtM) (Active)

| Notice to Mariners Ref. | Date of Issue | Activity (Vessel in brackets)                                      | Status of Works | Expected close out   |
|-------------------------|---------------|--|-----------------|----------------------|
| ROWF NTM009             | 10/03/2016    | Approval of Safety Zones   | Ongoing         | June 2018            |
| ROWF NTM016             | 27/05/2016    | Installation Rock Pads   | Ongoing         | June 2018            |
| ROWF NTM017             | 24/06/2016    | Installation Rock Pads Round 2                                     | Ongoing         | June 2018            |
| ROWF NTM049             | 09/02/2017    | Safe distances of all structures within Rampion Offshore Wind      | Ongoing         | Until further notice |
| ROWF NTM 071            | 23-08-2017    | Updated Main Array Hazard Area                                     | Ongoing         | Until further notice |
| ROWF NTM 075            | 02-11-2017    | Updated Export Cables Hazard areas                                 | Ongoing         | Until further notice |
| ROWF NTM 91             | 04-01-2018    | Rampion Notices to Mariners Update 2018                            | Ongoing         | Until further notice |
| ROWF NTM 94             | 01-02-2018    | Rampion Aids to Navigation   | Ongoing         | May 2018             |
| ROWF NTM 96             | 13-02-2018    | Rampion surface laid export cable & wet stored anchor wire. Update | Ongoing         | Until further notice |
| ROWF NTM 101            | 17-03-2018    | Service and Relocation of Wave Rider Buoys                         | Ongoing         | Until further notice |
| ROWF NTM 102            | 09-03-2018    | Installation of cable protection and rock berms                    | Planned         | 30-04-2018           |
| ROWF NTM 103            | 10-04-2018    | Service and Relocation of Wave Rider Buoys                         | Planned         | 15-05-2018           |

**Secretary of State has approved our application for statutory Safety Zones (08/03/16) during the construction of the Rampion Wind Farm. These Safety Zones are defined as:**

- 500m around all structures (where construction vessels are present)
- 50m around all structures (whilst personnel are working on them) including the offshore substation.

All project vessel masters and 3<sup>rd</sup> party sea users are requested to remain a minimum safe distance of 500m around each vessel. Project vessels are to keep a sharp lookout (Radar/AIS and visual) for non-project vessels entering these zones and report to Duty MC via VHF P1 ASAP.

### 2) Hazards/Mitigation for Project Vessels and PAX

- GSK pipeline



# Weekly Notice of Operations (WNoO)

## Rampion Offshore Wind Farm Limited Construction Operations

Issue Date: 13/04/2018 RAM-ERA-LOG-NOT-0001\_112  
- Weekly Notice of Operations

- 30m Safety Zone either side of the GSK pipeline situated to the East of the export cable corridor. No project vessels will be permitted to enter this safety zone without prior permission by the Duty MC
- Redundant sewage outfall pipeline
  - 30m Safety Zone either side of the redundant sewage outfall pipeline to the west of the cable route
- Fishing gear
  - All Vessels to keep a sharp lookout and report any fishing gear to duty MC who will in turn distribute information to all other project vessels.
  - All vessels to operate appropriately where the hazard of fishing gear exists
- Fishing vessels
  - Standing order for all project vessels to pass at a safe distance.
- Dive Vessels/Divers
  - Standing order for all project vessels to pass at a safe distance
  - Specifically, if any vessel is present over a known dive site, project vessels are to pass a minimum of 1NM uptide.
- Scour protection and exposed cables on sea bed around foundations
  - Guard vessel in operation
  - Co-ordinates disseminated to FLOs
- Subsea cables (buried, shallow buried and surface laid).
  - All project vessels to keep a sharp lookout for third party sea users venturing near subsea cables laid on sea bed. Report any such instances to Traffic ASAP. Special consideration of the exposed cable at the jointing location (50 42.97'N, 000 17.88'W) and to the east of the Offshore Substation.

Refer to Documents RAM-ERA-SMG-SAF-0001\_00 (Guidelines for CTV operators on specific hazards)






- Ensure all project vessels have latest Office Site Chart (Check with Duty MC for latest Rev)

# Weekly Notice of Operations (WNoO)

Rampion Offshore Wind Farm Limited Construction Operations

Issue Date: 13/04/2018 RAM-ERA-LOG-NOT-0001\_112

- Weekly Notice of Operations








| Name                           | Flag | Call Sign/MMSI  | Contact Info   | L (m) | B (m) | D (m) | GT (t) | Contractor                | Status (Start)  | Picture   |
|--------------------------------|------|-----------------|----------------|-------|-------|-------|--------|---------------------------|---|---|
| <b>3) Construction Vessels</b> |      |                 |                |       |       |       |        |                           |   |   |
| Nordness                       | (NL) | PHOG/244962000  | VHF<br>CH16/P1 | 166   | 24.5  | 6.8   | 18226  | Van Oord                  | Rock placement/cable protection. Start operations 17/04/18 weather permitting |    |
| Grand Canyon                   | (PA) | 3EVR8/370505000 | VHF<br>CH16/P1 | 125   | 30    | 6.6   | 18226  | VBMS                      | Burial export cable CR3 from KP5.4 to OSP                                     |    |
| Survey Vessel                  |      |                 |                |       |       |       |        |                           |   |   |
| Rix Tiger                      | (UK) | 2GGY4/235097309 | VHF<br>CH16/P1 | 19    | 9     | 1.8   | 42     | Rix Sea Shuttle           | Survey vessel<br>01/01/2018   |    |
| <b>4) Guard Vessels</b>        |      |                 |                |       |       |       |        |                           |   |   |
| George Johannes                | (UK) | MCPF5/232006450 | VHF<br>CH16/P1 | 26.27 | 6.48  | 3.2   | 122    | Choice Marine             | Guard Boat Duties 24/7<br>Start 30/07/2017                                    |   |
| Commodore P                    | (UK) | 2GIR2/235097729 | VHF<br>CH16/P1 | 18    | 6     | 0.9   | 27     | Offshore Turbine Services | Fast Response Guard Vessel<br>Start 18/08/2017                                |  |

# Weekly Notice of Operations (WNoO)

Rampion Offshore Wind Farm Limited Construction Operations

Issue Date: 13/04/2018 RAM-ERA-LOG-NOT-0001\_112

- Weekly Notice of Operations

| Name                            | Flag | Call Sign/MMSI  | Contact Info | L (m) | B (m) | D (m) | GT (t) | Contractor                 | Status (Start)  | Picture  |
|---------------------------------|------|-----------------|--------------|-------|-------|-------|--------|----------------------------|---|--|
| <b>5) Crew Transfer Vessels</b> |      |                 |              |       |       |       |        |                            |   |  |
| Windcat 6                       | (UK) | MXFD/235057789  | VHF CH 16/P1 | 16    | 6     | 2     | 40     | Windcat                    | Site CTV<br>Working out of Newhaven                       |   |
| Windcat 10                      | (UK) | 2BAN2/235064453 | VHF CH16/P1  | 22    | 6     | 2     | 36     | Windcat                    | WTG M&E completion<br>Working out of Newhaven             |   |
| Brava                           | (DK) | OUYP2/219017205 | VHF CH16/P1  | 21    | 7     | 2.3   | 118    | Northern Offshore Services | OSP CTV Start<br>19/03/2018                               |   |
| Porth Nefyn                     | (UK) | 2IRQ8/235112231 | VHF CH 16/P1 | 19    | 8     | 1.6   | 48     | Turbine Transfers          | Crew change / Water taxi<br>11/03/2017                    |   |
| Windcat 22                      | (UK) | 2CUS9/235075935 | VHF CH16/P1  | 22    | 6.5   | 2.1   | 40     | Windcat                    | O&M Vessel<br>Working out of Newhaven<br>Start 29/01/2017 |   |
| CWIND SWORD                     | (UK) | 2IAE5/235108046 | VHF CH 16/P1 | 22    | 6     | 1.8   | 35     | C-Wind                     | O&M CTV Start<br>13/11/2017                               |   |
| Windcat 14                      | UK   | 2BS19/235070403 | VHF CH 16/P1 | 18    | 6     | 1.9   | 40     | Windcat                    | O&M Vessel<br>Working out of Newhaven<br>Start 01/04/2018 |  |



# Weekly Notice of Operations (WNoO)

## Rampion Offshore Wind Farm Limited Construction Operations

Issue Date: 13/04/2018 RAM-ERA-LOG-NOT-0001\_112  
- Weekly Notice of Operations

### 6) Upcoming Operations (following 7 days)

| Operation                                       | Location  | Vessel                         | Operational Notes   |
|---|---|--------------------------------|---|
| Burial of export cable C3                       | Export cable route from KP5.4 to OSP as per NTM 00103 | Grand Canyon                   | Planned to start 22.04.18 and last approx. 1-week weather permitting  |
| Installation of cable protection and rock berms | Array/export and offshore substation as per NTM 00102 | Nordnes                        | Planned to start 16.04.18 and last approx. 2 weeks weather permitting |
| Snagging<br>Painting                            | All locations   | Windcat 6                      | Ongoing   |
| Crew change<br>Water Taxi                       | All Locations/Newhaven Port                           | Porth Nefyn                    | Ongoing   |
| Project Guard vessels                           | Site 24hr Guard Vessels                               | George Johannes, Commodore P,  | Ongoing   |
| Survey  | Multibeam/side scan surveys/IOW                       | Rix Tiger                      | Ongoing   |
| OSS works                                       | Offshore sub station                                  | Brava,                         | Ongoing   |
| O&M Vessels                                     | All locations   | WC 22<br>C-Wind Sword<br>WC 14 | ongoing   |

**All Mariners Operating in the Vicinity of Rampion Offshore Wind Farm are advised to familiarise themselves with MGN 372**  
[https://www.gov.uk/government/uploads/system/uploads/attachment\\_data/file/440734/MGN\\_372.pdf](https://www.gov.uk/government/uploads/system/uploads/attachment_data/file/440734/MGN_372.pdf)

### 7) Summary of Operations (previous 7 days)

- Guard vessel offshore 24/7
- MVOW mechanical completions/commissioning.
- Ongoing surveys
- Complete CR3 installation (Burial still to be completed)

### 8) Looking further ahead (beyond 7 days) (new activities starting)

- Array cable protection
- Export cable protection and burial
- Complete commissioning of WTG's
- Installation of CR4 export cables
- Arrival of OSP Work platform
- Change over to operational Aids to Navigation
- Removal of 6 x Cardinals and repositioning remaining North and South to permanent positions
- Dive operations on the nearshore CR3



# Weekly Notice of Operations (WNoO)

## Rampion Offshore Wind Farm Limited Construction Operations

Issue Date: 13/04/2018 RAM-ERA-LOG-NOT-0001\_112  
- Weekly Notice of Operations

### 9) Project Met mast details

| ID       | Latitude    | Longitude  |
|----------|-------------|------------|
| Met mast | 50°41.287'N | 0°20.594'W |

### 10) Project Wave Rider

Wave Riders 1 & 3 have been moved to the below as laid positions. All 3 x buoys have been serviced and the NAV aids are operational.

| ID                 | Latitude    | Longitude  |
|--------------------|-------------|------------|
| Wave Rider 1 KP 5  | 50°46.546'N | 0°18.862'W |
| Wave Rider 2 EOS   | 50°41.396'N | 0°16.147'W |
| Wave Rider 3 Array | 50°40.061'N | 0°12.194'W |

### 11) As Laid Cardinal Buoy Positions

| Cardinal Name | Light Signature  | Deployed Latitude | Deployed Longitude |
|---------------|------------------|-------------------|--------------------|
| North 1(AIS)  | Q                | 50° 41.377'N      | 0° 21.898'W        |
| North 2       | V Q              | 50° 42.072'N      | 0° 17.098'W        |
| North 3 (AIS) | Q                | 50° 42.771'N      | 0° 12.286'W        |
| East 1        | Q (3) 10s        | 50° 41.050'N      | 0° 11.311'W        |
| South 1(AIS)  | Q (6) + L Fl 15s | 50° 39.172'N      | 0° 11.363'W        |
| South 2       | V Q (6)+L Fl 10s | 50° 38.398'N      | 0° 16. 147'W       |
| South 3 (AIS) | Q (6) + L Fl 15s | 50° 37.631'N      | 0° 20.931'W        |
| West 1        | Q (9) + 15s      | 50° 39.439'N      | 0° 21.930'W        |

### 12) Contact details

#### Mark Brown

Offshore Site Manager

Tel: +44 (0) 7491 057 121

Email: [mark.brown@eon.com](mailto:mark.brown@eon.com)

#### Gordon Bain

Lead Marine Coordinator

Tel: +44 (0) 7816 648082

Email: [leadmc@rampionoffshore.com](mailto:leadmc@rampionoffshore.com).

#### Duty Marine Coordinator

Tel: +44 (0) 7557 942945

Email: [traffic@rampionoffshore.com](mailto:traffic@rampionoffshore.com)





# Weekly Notice of Operations (WNoO)

## Rampion Offshore Wind Farm Limited Construction Operations

Issue Date: 13/04/2018 RAM-ERA-LOG-NOT-0001\_112  
- Weekly Notice of Operations

### 13) Export Cable Coordinates

This is **CR1 west** cable RPL

| KP     | WGS84 Latitude | WGS84 Longitude |
|--------|----------------|-----------------|
| 0.000  | 50°49.0393'N   | 0°20.1560'W     |
| 0.006  | 50°49.0365'N   | 0°20.1542'W     |
| 0.415  | 50°48.8321'N   | 0°20.0213'W     |
| 1.019  | 50°48.5312'N   | 0°19.8257'W     |
| 3.030  | 50°47.5284'N   | 0°19.1741'W     |
| 4.184  | 50°46.9242'N   | 0°18.9366'W     |
| 4.284  | 50°46.8710'N   | 0°18.9224'W     |
| 4.718  | 50°46.6378'N   | 0°18.8890'W     |
| 4.818  | 50°46.5839'N   | 0°18.8887'W     |
| 5.791  | 50°46.0611'N   | 0°18.9566'W     |
| 6.978  | 50°45.4303'N   | 0°19.1314'W     |
| 7.171  | 50°45.3274'N   | 0°19.1549'W     |
| 7.272  | 50°45.2733'N   | 0°19.1603'W     |
| 7.439  | 50°45.1831'N   | 0°19.1583'W     |
| 7.631  | 50°45.0808'N   | 0°19.1341'W     |
| 8.901  | 50°44.4092'N   | 0°18.9209'W     |
| 9.225  | 50°44.2370'N   | 0°18.8761'W     |
| 9.635  | 50°44.0189'N   | 0°18.8193'W     |
| 10.165 | 50°43.7400'N   | 0°18.7177'W     |
| 10.718 | 50°43.4532'N   | 0°18.5891'W     |
| 10.994 | 50°43.3127'N   | 0°18.5123'W     |
| 11.094 | 50°43.2635'N   | 0°18.4778'W     |
| 11.227 | 50°43.2008'N   | 0°18.4232'W     |
| 11.327 | 50°43.1559'N   | 0°18.3757'W     |
| 11.733 | 50°42.9854'N   | 0°18.1587'W     |
| 12.179 | 50°42.8177'N   | 0°17.8873'W     |
| 13.356 | 50°42.4145'N   | 0°17.1150'W     |
| 13.629 | 50°42.3213'N   | 0°16.9363'W     |
| 14.751 | 50°41.9243'N   | 0°16.2157'W     |
| 15.573 | 50°41.6652'N   | 0°15.6499'W     |
| 15.641 | 50°41.6359'N   | 0°15.6168'W     |
| 15.751 | 50°41.5783'N   | 0°15.5962'W     |

This is **CR3 east** cable RPL (CR2 replacement)

| KP     | WGS84 Latitude | WGS84 Longitude |
|--------|----------------|-----------------|
| 0.000  | 50°49.0411'N   | 0°20.1492'W     |
| 0.006  | 50°49.0384'N   | 0°20.1472'W     |
| 0.401  | 50°48.8450'N   | 0°20.0043'W     |
| 1.019  | 50°48.5436'N   | 0°19.7817'W     |
| 3.097  | 50°47.5283'N   | 0°19.0324'W     |
| 4.003  | 50°47.0635'N   | 0°18.7953'W     |
| 4.505  | 50°46.7967'N   | 0°18.7217'W     |
| 4.757  | 50°46.6611'N   | 0°18.7071'W     |
| 5.759  | 50°46.1220'N   | 0°18.7677'W     |
| 7.114  | 50°45.4019'N   | 0°18.9671'W     |
| 7.222  | 50°45.3444'N   | 0°18.9758'W     |
| 7.321  | 50°45.2910'N   | 0°18.9770'W     |
| 7.439  | 50°45.2273'N   | 0°18.9702'W     |
| 10.026 | 50°43.8559'N   | 0°18.5656'W     |
| 10.633 | 50°43.5372'N   | 0°18.4469'W     |
| 10.884 | 50°43.4091'N   | 0°18.3785'W     |
| 11.055 | 50°43.3249'N   | 0°18.3183'W     |
| 11.214 | 50°43.2519'N   | 0°18.2483'W     |
| 11.313 | 50°43.2087'N   | 0°18.1987'W     |
| 11.443 | 50°43.1551'N   | 0°18.1270'W     |
| 11.704 | 50°43.0495'N   | 0°17.9807'W     |
| 11.949 | 50°42.9493'N   | 0°17.8447'W     |
| 12.083 | 50°42.8969'N   | 0°17.7662'W     |
| 12.146 | 50°42.8475'N   | 0°17.6541'W     |
| 12.248 | 50°42.8757'N   | 0°17.7250'W     |
| 13.450 | 50°41.9365'N   | 0°15.9714'W     |
| 14.848 | 50°41.7608'N   | 0°15.6987'W     |
| 15.306 | 50°41.7048'N   | 0°15.6218'W     |
| 15.444 | 50°41.7048'N   | 0°15.6218'W     |
| 15.468 | 50°41.6938'N   | 0°15.6095'W     |
| 15.486 | 50°41.6857'N   | 0°15.6021'W     |
| 15.511 | 50°41.6733'N   | 0°15.5939'W     |
| 15.536 | 50°41.6603'N   | 0°15.5884'W     |
| 15.561 | 50°41.6469'N   | 0°15.5855'W     |
| 15.586 | 50°41.6334'N   | 0°15.5854'W     |
| 15.691 | 50°41.5770'N   | 0°15.5934'W     |





# Weekly Notice of Operations (WNoO)

## Rampion Offshore Wind Farm Limited Construction Operations

Issue Date: 13/04/2018 RAM-ERA-LOG-NOT-0001\_112  
- Weekly Notice of Operations

FO RPL as follows:

| KP     | WGS84 Latitude | WGS84 Longitude |
|--------|----------------|-----------------|
| 0.000  | 50°49.0288'N   | 0°20.1448'W     |
| 0.278  | 50°48.8916'N   | 0°20.0492'W     |
| 1.211  | 50°48.4311'N   | 0°19.7300'W     |
| 2.087  | 50°47.9985'N   | 0°19.4300'W     |
| 2.282  | 50°47.9126'N   | 0°19.3346'W     |
| 2.980  | 50°47.5715'N   | 0°19.0830'W     |
| 3.978  | 50°47.0594'N   | 0°18.8217'W     |
| 4.476  | 50°46.7947'N   | 0°18.7488'W     |
| 4.724  | 50°46.6612'N   | 0°18.7343'W     |
| 5.722  | 50°46.1242'N   | 0°18.7948'W     |
| 7.077  | 50°45.4043'N   | 0°18.9941'W     |
| 7.187  | 50°45.3453'N   | 0°19.0030'W     |
| 7.289  | 50°45.2905'N   | 0°19.0041'W     |
| 7.410  | 50°45.2251'N   | 0°18.9973'W     |
| 10.000 | 50°43.8523'N   | 0°18.5922'W     |
| 10.609 | 50°43.5324'N   | 0°18.4731'W     |
| 10.863 | 50°43.4028'N   | 0°18.4038'W     |
| 11.038 | 50°43.3168'N   | 0°18.3424'W     |
| 11.200 | 50°43.2422'N   | 0°18.2709'W     |
| 11.596 | 50°43.0527'N   | 0°18.1163'W     |
| 11.743 | 50°42.9910'N   | 0°18.0375'W     |
| 12.025 | 50°42.8797'N   | 0°17.8742'W     |
| 12.316 | 50°42.7828'N   | 0°17.6795'W     |
| 13.472 | 50°42.4242'N   | 0°16.8768'W     |
| 14.868 | 50°41.9239'N   | 0°15.9902'W     |
| 15.414 | 50°41.7145'N   | 0°15.6650'W     |
| 15.469 | 50°41.6927'N   | 0°15.6328'W     |
| 15.580 | 50°41.6382'N   | 0°15.5972'W     |
| 15.671 | 50°41.5891'N   | 0°15.5942'W     |
| 15.690 | 50°41.5771'N   | 0°15.5934'W     |



# Weekly Notice of Operations (WNoO)

## Rampion Offshore Wind Farm Limited Construction Operations

Issue Date: 13/04/2018 RAM-ERA-LOG-NOT-0001\_112  
- Weekly Notice of Operations

### 14) New Proposed CR4 Export Cable Coordinates

| Latitude       | Longitude     | KP     |
|----------------|---------------|--------|
| 50° 49.0347' N | 0° 20.1759' W | 0.000  |
| 50° 48.8174' N | 0° 20.0679' W | 0.422  |
| 50° 48.499' N  | 0° 19.9179' W | 1.038  |
| 50° 47.5073' N | 0° 19.2754' W | 3.026  |
| 50° 46.9104' N | 0° 19.0408' W | 4.167  |
| 50° 46.8624' N | 0° 19.028' W  | 4.257  |
| 50° 46.6346' N | 0° 18.9954' W | 4.681  |
| 50° 46.5865' N | 0° 18.9951' W | 4.770  |
| 50° 46.0698' N | 0° 19.0621' W | 5.732  |
| 50° 45.4367' N | 0° 19.1944' W | 6.916  |
| 50° 45.3316' N | 0° 19.2183' W | 7.113  |
| 50° 45.2744' N | 0° 19.2241' W | 7.219  |
| 50° 45.1798' N | 0° 19.222' W  | 7.394  |
| 50° 45.0737' N | 0° 19.1969' W | 7.593  |
| 50° 44.4019' N | 0° 18.9836' W | 8.864  |
| 50° 44.2304' N | 0° 18.939' W  | 9.186  |
| 50° 44.011' N  | 0° 18.8819' W | 9.598  |
| 50° 43.7299' N | 0° 18.7794' W | 10.133 |
| 50° 43.441' N  | 0° 18.6499' W | 10.690 |
| 50° 43.2979' N | 0° 18.5716' W | 10.971 |
| 50° 43.2454' N | 0° 18.5349' W | 11.078 |
| 50° 43.1797' N | 0° 18.4776' W | 11.217 |
| 50° 43.1319' N | 0° 18.4271' W | 11.324 |
| 50° 42.958' N  | 0° 18.2059' W | 11.738 |
| 50° 42.7875' N | 0° 17.9298' W | 12.191 |
| 50° 42.3833' N | 0° 17.1555' W | 13.372 |
| 50° 42.2907' N | 0° 16.9781' W | 13.642 |
| 50° 41.9023' N | 0° 16.2441' W | 14.767 |
| 50° 41.796' N  | 0° 16.0069' W | 15.109 |
| 50° 41.6474' N | 0° 15.666' W  | 15.596 |
| 50° 41.6235' N | 0° 15.6358' W | 15.653 |
| 50° 41.5764' N | 0° 15.5982' W | 15.751 |




# Weekly Notice of Operations (WNoO)

## Rampion Offshore Wind Farm Limited Construction Operations

Issue Date: 13/04/2018 RAM-ERA-LOG-NOT-0001\_112  
- Weekly Notice of Operations

### 15) Site Chart

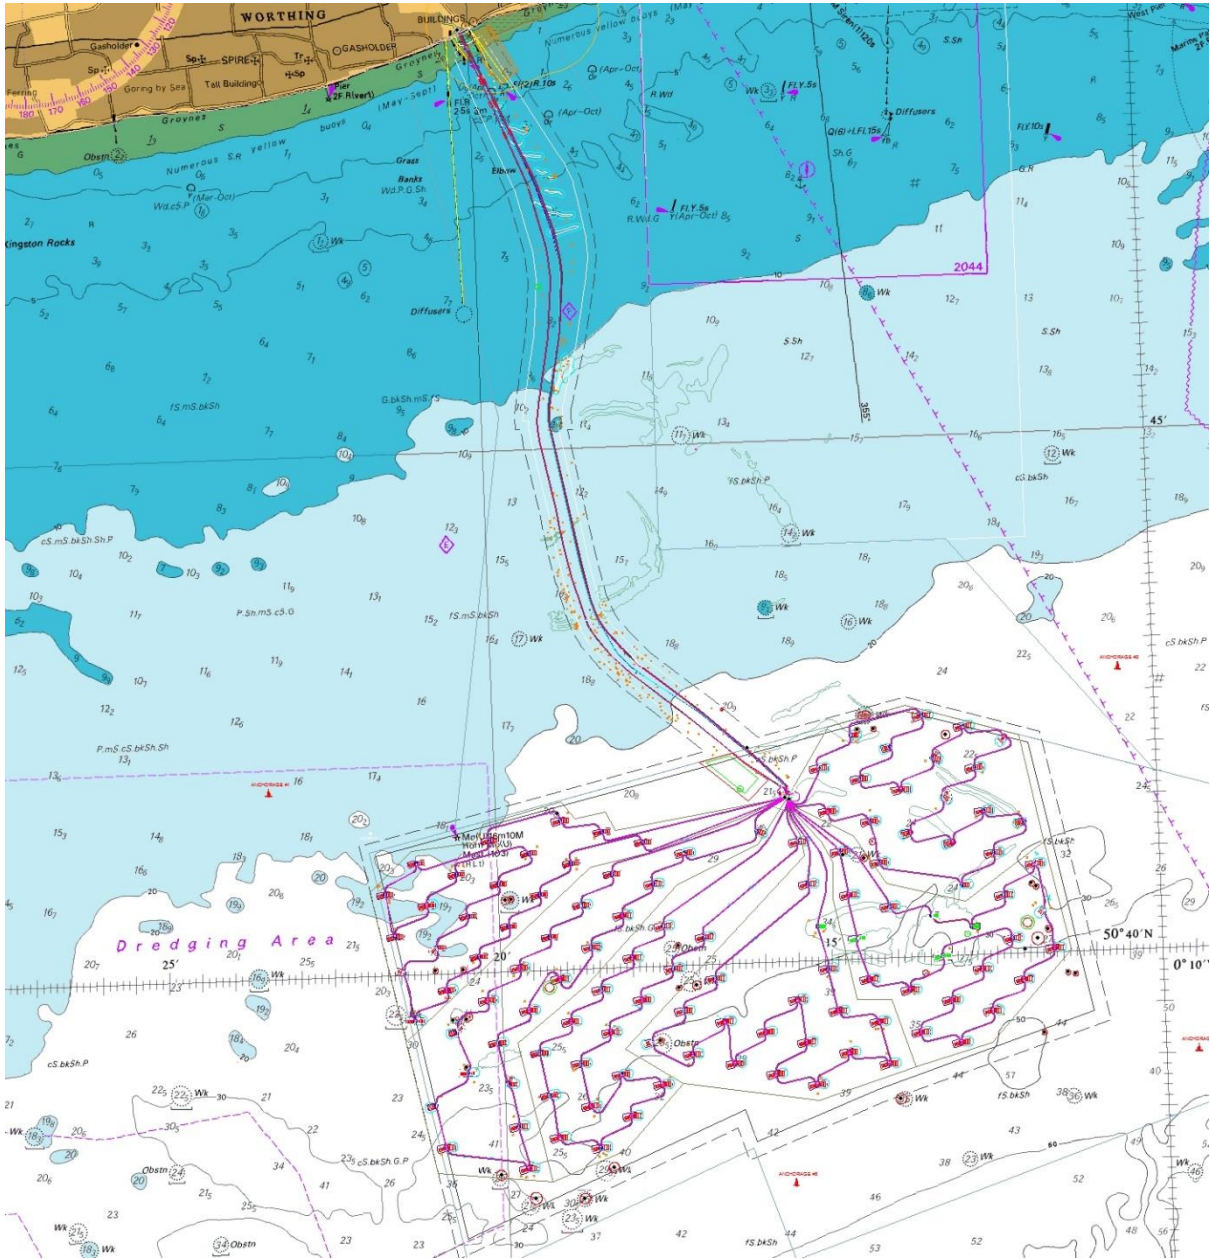

# Weekly Notice of Operations (WNoO)

## Rampion Offshore Wind Farm Limited Construction Operations

Issue Date: 13/04/2018 RAM-ERA-LOG-NOT-0001\_112  
- Weekly Notice of Operations

16) Surface laid export cable and wet stored anchor wire details see update NTM 0096

**Anchor wire has been removed.**

